

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Student Information

- **Student Name:** Adarsha E
- **SRN:** PES1UG24AM334
- **Section:** F

1. Lab Objective


Convert functional requirements from Lab 1 into Agile backlog items (Epics and User Stories), prioritize and estimate them using the Fibonacci sequence (Planning Poker), simulate a 1-week sprint across workflow states (To Do → In Progress → Done), and analyze team progress and velocity using Jira's Burndown Chart.

2. Lab Deliverables & Screenshots

Deliverable 1: Jira Backlog with Epics and User Stories


ID	Type	Summary	Parent Epic	Priority	Story Points
AM334-1	Epic	Loyalty Wallet & Point Aggregation	—	High	—
AM334-2	Epic	Point Conversion & Exchange	—	High	—
AM334-3	Epic	Gift Card Redemption & Anti-Fraud	—	High	—

AM334-4	Epic	Merchant Partner Management	—	Medium	—
AM334-6	Story	Link Merchant Loyalty Program	Loyalty Wallet & Point Aggregation	High	5
AM334-7	Story	Validate Merchant Loyalty Points	Point Conversion & Exchange	High	3
AM334-8	Story	Apply Dynamic Exchange Rate	Point Conversion & Exchange	High	5
AM334-9	Story	Convert Loyalty Points to Exchange Credits	Point Conversion & Exchange	High	5
AM334-10	Story	Browse Available Gift Cards	Gift Card Redemption & Anti-Fraud	Medium	3
AM334-11	Story	Redeem Gift Card Using Exchange Credits	Gift Card Redemption & Anti-Fraud	High	8
AM334-12	Story	Lock Voucher Against Duplicate Redemption	Gift Card Redemption & Anti-Fraud	High	8
AM334-13	Story	Handle Redemption Failure	Gift Card Redemption & Anti-Fraud	High	5
AM334-14	Story	Manage Gift Card Catalog	Merchant Partner Management	Medium	5
AM334-15	Story	Publish Loyalty Program	Merchant Partner Management	Medium	5
AM334-16	Story	View Gift Card Redemption Reports	Merchant Partner Management	Medium	3
TOTAL	4 Epics + 11 Stories				55

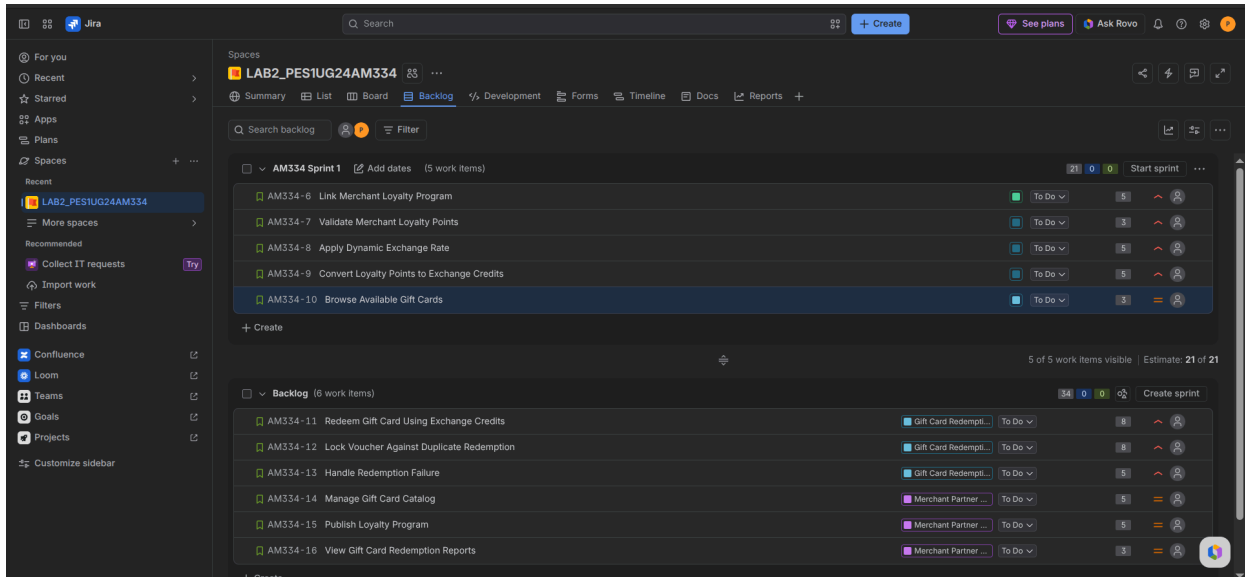


Deliverable 2: Active Sprint Board (Sprint Simulation)

Sprint 1:

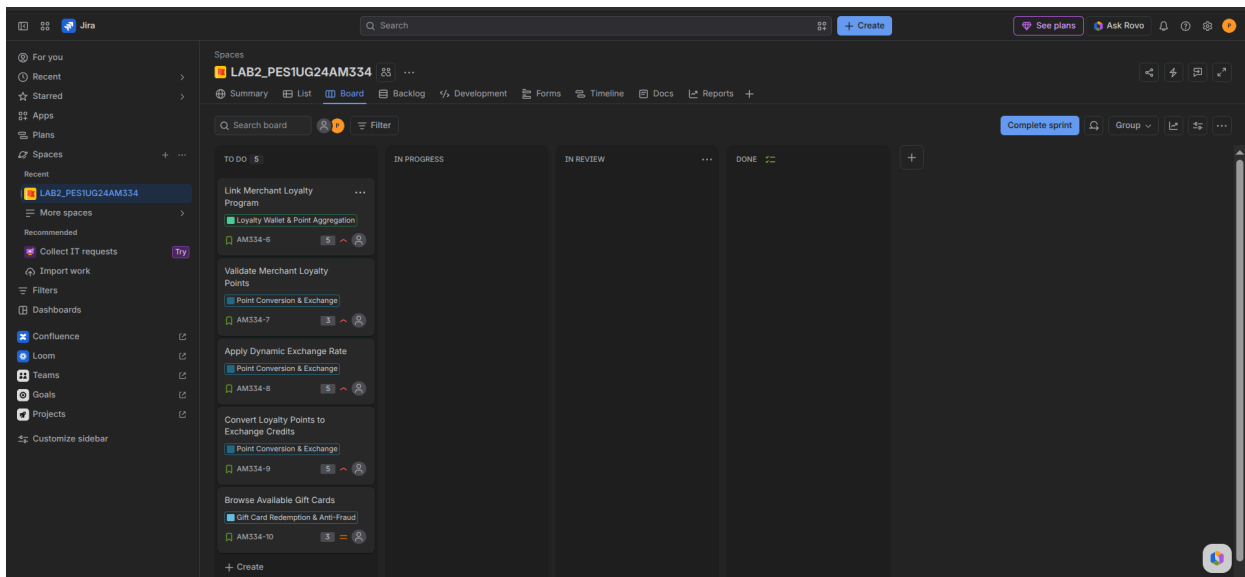

Sprint 2:

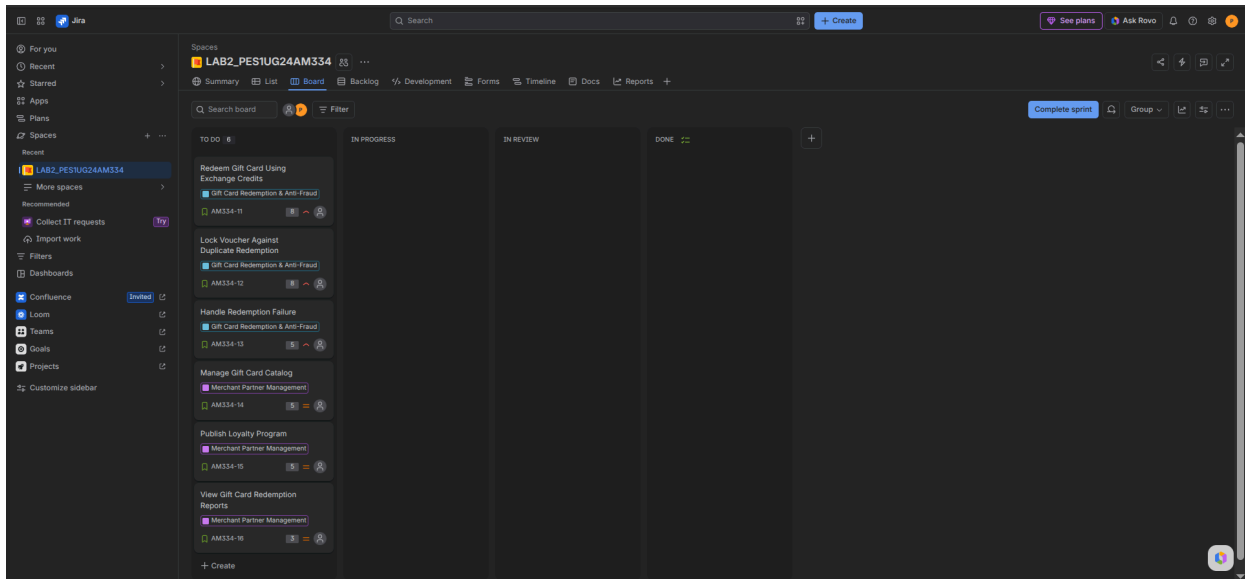


Deliverable 3: Sprint Burndown Chart

Sprint 1:



Sprint 2:

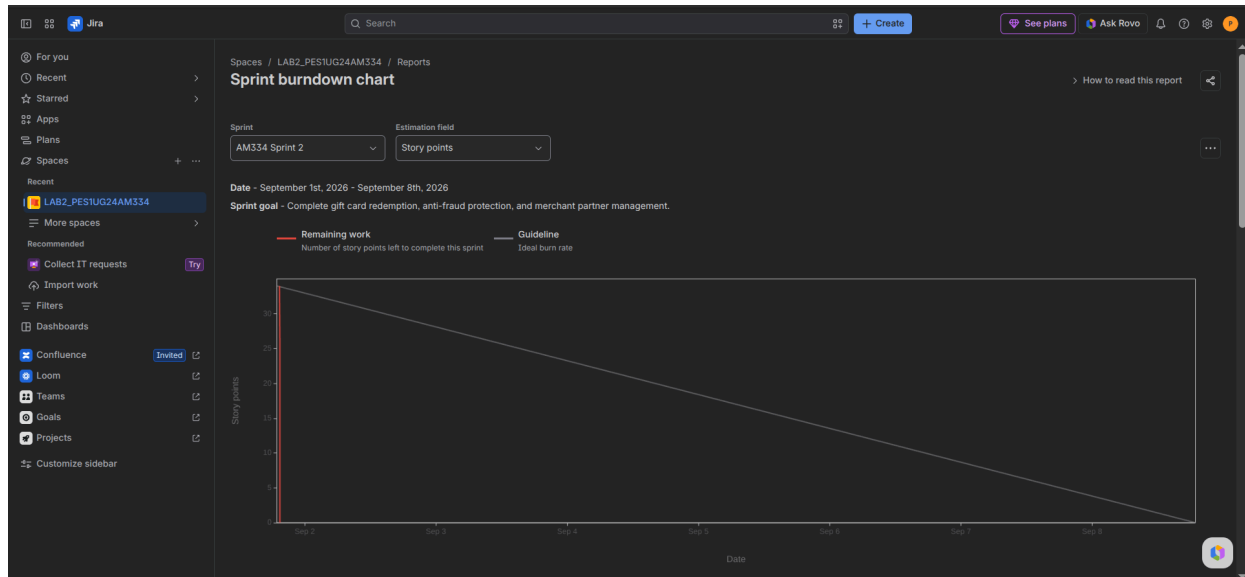

4. Sprint Reflection & Analysis

1. Did your estimations reflect the actual effort?

Answer: Yes. The story-point estimates reasonably reflected the relative effort and complexity of the work. Smaller tasks such as validating loyalty points and viewing redemption reports were assigned 3 points, while moderately complex tasks were assigned 5 points. Larger workflows such as gift-card redemption and voucher locking were assigned 8 points because they involve multiple dependent operations.

2. Was your backlog well-prioritized?

Answer: Yes. The backlog was prioritized according to the importance of the functionality. High-priority features such as loyalty-point validation, exchange-rate application, point conversion, gift-card redemption, and anti-fraud protection were placed before medium-priority features such as gift-card browsing, catalog management, loyalty-program publishing, and redemption reporting.

3. How did your simulated sprint align with your plan?

Answer: The simulated sprints followed the planned development flow.

Sprint 1 focused on the core loyalty wallet and point-conversion functionality, while **Sprint 2** focused on gift-card redemption, anti-fraud

protection, and merchant partner management. The stories were moved through **To Do → In Progress → In Review → Done**, allowing the planned sprint workflow to be demonstrated.

4. **What insights did the burndown chart give about your team's capacity?**

Answer: The burndown chart showed how the remaining story points decreased as work items were completed. Sprint 1 contained **21 story points**, while Sprint 2 contained **34 story points**. Since the sprints were simulated for the lab, the work was completed much faster than it would be in a real development sprint. The chart therefore demonstrated the relationship between completed work, remaining workload, and planned team capacity rather than representing actual development velocity.
